Case Number: WLS 2011-01132

BUNCOMBE COUNTY HEALTH CENTER
ENVIRONMENTAL HEALTH SERVICES (828-250-5016)
OPERATIONS PERMIT

PIN: 9745700146.00

Property Owner: Echoview Community Mill Property Location: Jupiter Rd Application Date: 12-15-11

Directions: I-26 W to Exit 15 (L) on Jupiter Rd. .4mi on (L)

Subdivision: _____ Phase/section: _____ Lot# _____ Installer: Andy Brown

Water Supply: ☒ Private Well ☐ Spring ☐ Shared Well ☐ Community Min. Required Separation Distance 100' Installed ? ☒ Yes ☐ No

Conditions: 1) Pump septic tank every 3 to 5 years. **2)** Divert all gutters and other surface water, away from septic system and repair areas. **(3)** No cutting or filling over septic system and repair areas.

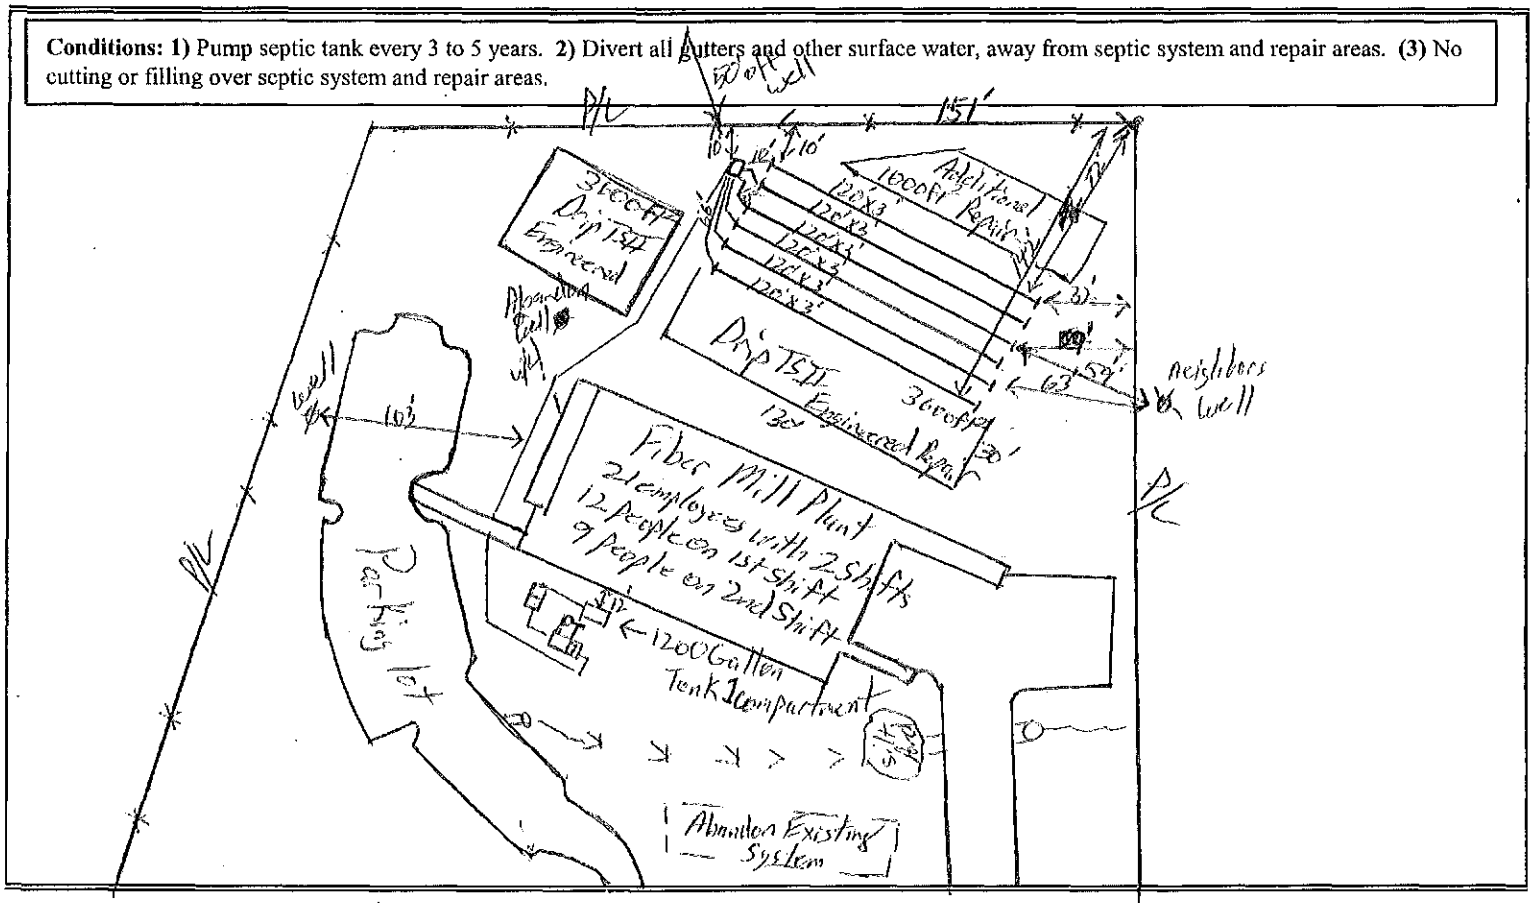

Operations Permit For: ☒ New System ☐ Repair ☐ Revision Drawings, plans, conditions, etc. attached? ☐ Yes ☐ No

System Approved For: ☒ House ☐ Mobile Home (☐ single ☐ double) Bedrooms: _____ Basement: ☐ Yes ☐ No Basement Plumbing: ☐ Yes ☐ No

☐ Multiple Unit Dwelling: No. of Units _____ Number of Bedrooms per unit _____ ☐ Business No. Employees: _____ No: Shifts: _____

Operation Description: Fiber Mill Plant total employees = 21 with 2 shifts 1st shift - 12 Employees 2nd Shift = 9 Employees Industrial Waste: Yes ☐ No ☐
Tour Groups = 25 people per day

Approved Installation Specifications: *Total Design Flow:* 875 (GPD) *LTAR:* .30 *System Classification:* Type I__, II__, III g, IV__, V__, VI__

Pump System Required: ☒ Yes ☐ No *Pump Specification* Pump Make: Goulds Model: ½ HP Serial No. _____

Trenches: Length: 720 ft No. of Trenches 6 Width: 36 Spacing: 9 ft Depth: 24 in (lower sidewall) Stone Depth: ___ in

Distribution: ☒ Equal Gravity ☐ Pressure Manifold ☐ Serial ☐ Dams/Step Downs *Tank Size:* Septic: 1-1000 1-1200 (gallons) Pump Tank: 1000 (gallons)

System Description: ☐ Prefabricated Panel Block ☐ Conventional ☐ Large Diameter Pipe ☐ Chamber ☒ Expanded Polystyrene Aggregate ☐ Other _____

Comments: _____

Inspected by: [signature] Date: 3-7-12 Issued To: [signature] Date 3/7/12

The system has been installed in accordance with state sewage rules. Approval does not guarantee the system will function satisfactory for any given time.

Operprmt.doc.rev 03/05/04
